



Gobierno de
Colombia



2022

**EUTF Colombia
6TH ANNUAL REPORT TO THE
MANAGEMENT BOARD**

European Union Trust Fund

Website: <https://www.fondoeuropeoparalapaz.eu/>

We thank all the projects financed through the EUTF for their collaboration and the provision of photographic material for the preparation of this report.

Table of contents

1. Policy and operational highlights of the year	4
1.1 Policy and operational highlights	4
1.2 Summary of programmes adopted and current pipeline	5
1.3 Obstacles encountered	6
1.4 Particular risks associated with the management of EUTF programmes	6
2. Programming, implementation and results, including evaluations	7
2.1 Brief description of programmes adopted	7
2.2 Monitoring and lessons learnt	7
2.3 Main achievements of the EUTF	8
3. Financial report	21
3.1 Amounts pledged and received	21
3.2 Amounts paid	21
3.3 Beneficiaries and amounts contracted	22
4. Management and internal control	23
4.1 Control results	23
4.1.1 Control effectiveness as regards legality and regularity	23
4.2 Observations and recommendations made by Internal Audit Service	23
4.3 Assessment of the effectiveness of the internal control systems / EU Court of Auditors	23
4.4 Conclusions as regards assurance	24
5. Declaration of assurance (and reservations)	25
6. Annexes:	26
Annex I: EUTF projects	27
Annex II. List of derogations, exceptions, non-compliance events, prior approvals and events to be reported	45
Annex III: List of EUTF Projects	46

1. Policy and operational highlights of the year

1.1. Policy and operational highlights

No Operational or Strategic committees were organised in 2022 due to the transitional nature of the political year with the change of governments.

Gustavo Petro's government has set out to make peace an overarching priority, seeking to achieve "Total Peace" in the country. This entails implementing the 2016 Peace Agreement in full, opening negotiations with the Ejército de Liberación Nacional (ELN) and building channels towards the many other armed groups active in Colombia. Ultimately, this also means solving social and territorial inequalities, which are the main reasons for the violence in the country. Political, technical, and financial support to the implementation of the Peace Agreement remains key for Colombia's Government.

During the new government's relatively long period of launching its political agenda, the EU and its Member States have maintained constant dialogue with National Agencies, which play an important role in peace activities. The EU together with EUMS are well placed to accompany peace efforts with short and long term measures, based on experience from e.g. the EU Trust Fund.

The EU Trust Fund has heavily contributed to the visibility and success of EU support to Colombia's peace efforts over the last six years. This innovative set-up allowed for efficient pooling of EU and EUMS resources, agility in formulating projects responding to the needs of the peace process both locally and nationally, and strong government involvement in project management. The EUTF has been widely appreciated by the Colombian government, participating EU and non-

EU states and beneficiaries, particularly rural communities and former combatants in reincorporation. The mechanism has developed its potential in terms of EU co-ordination, agility, visibility and political dialogue. Although implementation continues, no more funds have been added since 2021 and no further contracts have been signed, in line with the overall approach of phasing out trust funds and other ad-hoc financing instruments.

In depth strategic and legal discussions with EUMS and Government of Colombia on the EU future support to the peace process have led to the conclusion that a Team Europe Initiative provides a good basis for coordination and should continue to be pursued, but no other instrument provides the same level of political leverage and operational versatility as the EUTF.

Petro's election has led to a reconfiguration of Peace agencies and policies in the country. This process has affected EUTF interventions, particularly budget support, delaying disbursements, changing indicators and influencing policy dialogue. Land ownership as part of the Comprehensive Land Reform is a priority for Petro's Government. The newly appointed Director of the National Land Agency (ANT) has expressed the need to speed up the process of land formalisation with digital technologies and to ensure a stronger state presence in the territories. This new requirements need to be adjusted in the complementary support that the EU is providing to the Agency.

Until the end of 2021, EU Member States, UK and Chile contributed with EUR 37 M, corresponding to 29 % of the total amount of the EUTF.

1.2. Summary of programmes adopted and current pipeline

No new programmes were adopted during 2022.

Six new contracts were signed during **2022** (T06.98, T06.99, T06.100, T06.101, T06.102, T06.104), for a total amount of **386.435 EUR**. Four contracts regard expenditure verification, one is an audit and one the mid-term evaluation.

Sixteen contracts were concluded until December 2022. On the 31st December 2022, the EUTF contained 36 ongoing contracts including the operational/audit and expenditure verification ones.

The current pipeline of ongoing projects are as follows:

Number	Title	Status	Start date of activity	Contracted amount (€)	Paid amount (€)	End date of activity
1	T06.2 Rutas para la Paz - Infivalle	EC	18/04/2017	1,128,903.84	1,128,903.84	01/07/2021
2	T06.4 EUTF "Mascapaz" - Instituto Sinchi	EC	08/06/2017	3,820,000.00	3,149,207.02	07/01/2024
3	T06.5 EUTF "Pazadentro" - Asociacion De Cabildos Nasa Cha Cha	EC	09/05/2017	2,100,000.00	2,054,338.26	08/12/2020
4	T06.7 Asistencia Técnica - DT GLOBAL IDEV EUROPE S.L	EC	08/11/2017	5,772,400.00	3,892,349.35	07/05/2024
5	T06.8 Territorios Caquetehños Sostenible Para la Paz - IVMF	EC	01/01/2018	3,775,965.00	3,345,216.97	30/06/2022
6	T06.9 Rural Paz - ICCO Cooperation	EC	15/02/2018	3,630,000.00	3,627,931.44	30/11/2021
7	T06.10 PUEDES - CISP	EC	30/12/2017	3,239,199.75	3,228,981.70	29/12/2021
8	T06.11 Implementación de acciones para la estabilización económica y social del municipio de puerto Guzmán- Putumayo	EC	01/05/2018	1,974,136.00	1,819,724.15	31/12/2021
9	T06.14 Amazonía Joven - Guaviare	EC	01/06/2018	2,627,730.00	2,619,822.49	31/10/2021
10	T06.20 PDT Nariño	EC	19/05/2018	6,500,000.00	6,499,991.00	18/03/2023
11	T06.23 Procesos de integración socioeconómica y colectiva como estrategia de dinamización comunitaria y construcción de paz	EC	19/05/2018	2,000,000.00	2,000,000.00	18/06/2021
12	T06.24 Caminemos	EC	12/06/2018	6,271,679.00	5,644,511.10	21/09/2022
13	T06.25 Humanicemos	EC	06/02/2020	4,000,000.00	3,884,088.91	05/07/2022
14	T06.28 Colombia PUEDE	EC	18/12/2018	5,400,000.00	2,692,348.50	17/09/2022
15	T06.29 SER putumayo	EC	24/11/2018	2,000,000.00	1,800,000.00	23/03/2022
16	T06.33 Constructores de paz	EC	16/01/2019	769,998.30	692,998.30	31/01/2023
17	T06.35 Economías Solidarias del Común	EC	14/12/2018	3,000,000.00	2,400,000.00	13/06/2023
18	T06.37 MIA	EC	11/04/2019	522,000.00	469,800.00	10/03/2023
19	T06.39 Comprehensive rural development for the promotion of sustainable peace	EC	06/09/2019	4,800,000.00	4,078,827.28	05/09/2023
20	T06.41 Empoderamiento político y económico territorial con enfoque en las mujeres rurales	EC	01/07/2019	6,340,000.00	4,590,000.00	31/03/2024
21	T06.60 Rutas PDET- Infraestructura	EC	18/07/2020	8,576,398.00	3,874,707.00	17/07/2024
22	T06.61 Rutas PDET- Cadenas	EC	01/08/2020	4,609,967.00	2,719,394.00	31/07/2024
23	T06.62 Rutas PDET- Innovacion	EC	23/12/2020	6,313,635.00	1,190,496.00	22/12/2024
24	T06.68 Contrato de ejecución de reforma sectorial de la política nacional sara la reincorporación social y económica (PNRSE) de las FARC-EP	EC	07/05/2020	10,980,000.00	8,480,000.00	06/05/2024
25	T06.73 Contrato de ejecución de reforma sectorial de la política de tierras: Tierras y Territorios Sostenibles para la paz	EC	23/12/2020	9,300,000.00	4,300,000.00	22/12/2024

Number	Title	Status	Start date of activity	Contracted amount (€)	Paid amount (€)	End date of activity	
26	T06.74	Apoyo complementario al contrato de ejecución de reforma sectorial "Tierras y Territorios Sostenibles para la Paz"	EC	03/06/2021	1,600,000.00	467,141.00	02/12/2024
27	T06.77	Asistencia técnica contrato de ejecución de reforma sectorial de la política nacional para la reincorporación social y económica (PNRSE) de exintegrantes de las FARC-EP	EC	02/12/2024	2,169,000.00	573,716.63	04/05/2024
28	T06.94	Piscicultura del Común - CISP	EC	09/09/2021	4,443,421.11	2,892,924.87	08/09/2024
29	T06.97	Escuela Taller, saberes y patrimonio para la paz	EC	15/12/2021	200,000.00	180,000.00	14/04/2023
30	T06.98	Audit of the EU Trust Fund Colombia	EC	02/02/2022	97,250.00	19,450.00	01/02/2027
31	T06.99	Verificación de gastos al contrato T06.29	EC	02/05/2022	18,710.00	0.00	01/05/2023
32	T06.100	Evaluación intermedia del Fondo Europeo para la Paz en Colombia	EC	18/05/2022	187,850.00	69,266.00	17/11/2022
33	T06.101	Verificación de gastos al contrato T06.2	EC	12/05/2022	29,074.00	29,074.00	11/09/2022
34	T06.102	Verificación de gastos al contrato T06.2 - ICCO	EC	01/02/2023	19,500.00	0.00	31/07/2023
35	T06.104	Verificación de gastos 2 lotes - Colombia	EC	20/03/2023	34,051.00	0.00	13/03/2024

1.3. Obstacles encountered

As in previous years, the **security situation** in many of the areas of intervention of the EUTF was a challenge for implementing partners. Threats against and assassination of social leaders, human rights defenders and former combatants affected the implementation of some of the projects. As before, this issue has been a regular topic in the dialogue between the Delegation and the Government of Colombia.

The government requested the neutralisation of two indicators of the Sector Reform Performance Contract "Land and Sustainable Territories for Peace", and the transfer of the corresponding amount to the next variable tranche of 2023. The government justified this request because of the increased insecurity and the presence of armed groups in the territory that had prevented the presence of the National Land Agency teams.

The transition period between the two governments, has affected EUTF implementation. The new government has taken time to appoint new directors of Peace Agencies, and they are still preparing for carrying out the "Total Peace" Policy.

1.4. Particular risks associated with the management of EUTF programmes

Parliamentary and Presidential elections in the first half of the year and the change of Government in August have distracted some partners, especially institutional ones, from implementation of projects or significant policy dialogue. Meanwhile, violence traditionally spikes around elections, posing additional challenges to implementing partners throughout the country.

2. Programming, implementation and results, including evaluations

2.1. Brief description of programmes adopted

No new programmes were adopted in 2022.

2.2. Monitoring and lessons learnt

The EUTF team carried out several monitoring field visits of projects during 2022.

Moreover, two projects received external “ROM” visits (Result Oriented Monitoring), which complemented the information submitted by implementing partners every three months.

In 2022, a mid-term evaluation of the EUTF was launched with the aim of generating inputs to guide further interventions; regarding the efficient use of resources and taking-stock of lessons learned that could be capitalised in constructing the Team Europe Initiative for Peace in Colombia. The analysis covered the period from the beginning of the EUTF’s operations in January 2017 until June 2022.

The evaluation coincided with the run-off of the presidential elections, limiting access to civil servants of the previous Government who had played a relevant role in the EUTF implementation.

The principal findings of the evaluation are the following:

- The Fund contributed to positioning the EU as a key political actor in the international community’s efforts to support the implementation of the Final Peace agreement.
- The EU political commitment, and the adaptability of the EUTF to respond to national priorities, clearly played a catalytic role in implementing the Peace Agreement. It also contributed to maintaining the validity of the Agreement, which has been under attack from political opponents since it came into force.
- The EUTF has been a valuable instrument for coordinating cooperation. The interventions supported by the EUTF have offered agile responses to the priority demands of the Government and target groups regarding compliance with Points 1 and 3.2 of the Peace Agreement, highlighting the relevance of projects strengthening the institutional response to reincorporation and access to land.
- The EUTF’s initial objectives gave it a wide-ranging and long-term mandate. The combination of far-reaching goals with actions focused on responding to immediate needs of ex-combatants returning to civilian life, gave rise to a complex portfolio of interventions not necessarily centred on a common strategy.
- The magnitude and complexity of structural reforms needed, widely surpasses responsibility and resources of international cooperation. As a result, interventions covered a wide range of target groups, geographical areas, activities and products. A specific Theory of Change and a corresponding chain of results would have enabled greater focus.
- The regular presence of the EUTF and high-level visits of diplomatic representatives,

offered political backing and a sense of protection for local actors committed to the peace process.

- The inclusion of different target groups in the same project created opportunities for dialogue and mutual understanding, increasing confidence between different actors and establishing foundations for reconciliation.
- The EUTF has systematically supported a differential approach focused on including youth, women and ethnic groups.
- The report highlights the need to differentiate short term measures, to respond to immediate needs of reincorporation, using humanitarian aid principles and strategies, with measures focused on medium and long-term reincorporation, which require longer time and greater articulation with the national and sectoral development plans.
- It is recommended to work with each implementing partner on exit strategies, indicating who will provide continuity to the activities, to ensure that the results obtained are maintained.
- It is suggested to provide continuity to the peace education efforts, and reinforce the communication strategy with El Espectador and community broadcasters articulating efforts to better disseminate initiatives carried out with the EUTF, around a common message of peace.
- The report underlines the need to stimulate the creation and signing of environmental preservation agreements in the territories where the EUTF intervenes to restore natural resources.

2.3. Main achievements of the EUTF

To obtain a consolidated overview of the EUTF actions, targets and results of the projects of the Trust Fund have been grouped in six main Strategic Pillars. Below, the main indicators and a short qualitative example for each Strategic Pillar are presented.





PILLAR 1: RECONCILIATION AND CONFLICT REDUCTION		Target	Progress
5.525	people strengthening capacities to promote tolerance and peaceful coexistence in their communities	3.835	>100%
12	local and territorial participation spaces receive technical assistance or support for Human Rights defense and peacebuilding actions	12	100%
3.550	people have participated in forums, events, or dialog spaces for peacebuilding, reconciliation, and strengthening of the territorial resources	610	>100%
385	people associated to community media have strengthened their social communication capacities for peacebuilding	375	>100%
44	community radio stations in municipalities affected by the armed conflict have increased their peacebuilding and reconciliation content	45	98%
4.445	people in the process of reincorporation and from nearby communities associated in common interest and mutual trust activities	5.030	88%

Reconciliation of indigenous population, victims, and peace signees in Caldon, Cauca

“The EUTF has supported a project aimed at reconciliation between excombatants and indigenous populations in the municipality of Caldon, Cauca”. This experience encouraged dialogue, and allowed the reconstruction of collective historical memory. Reconciliation exercises provided moments for emotional unloading, contributing to reduce prevailing tensions, ensuring mutual acknowledgement of parties in the conflict, and reaffirming willingness for reconciliation and non-repetition. One of the leaders of Cerro de Belén testifies: *“This exercise helped us to put words on the stories we had kept inside, and rememorize whatever was left of the conflict among young people, women, men, ex-combatants, people from indigenous councils, everyone. We rebuild a relation of peace and trust, and tried to leave behind the psychological damage, the imprint of the guerrilla”*. This experience brought tolerance and peaceful cohabitation and transformed the preconceived vision of Caldon, eliminating the stigma previously felt by the population.

Strengthening of Departmental and Municipal Boards for Effective Participation of Victims in Nariño

The EUTF implemented a capacity building strategy to ensure an Effective Participation of the Victims (MPEV) in the boards of the municipalities of Ipiales, Pasto, Tumaco and the Department of Nariño. The EUTF accompanied them in the elaboration of their work plans in alignment with departmental and municipal development plans, as well as encouraging advocacy actions regarding the assignment of public resources for their implementation. The Boards were equipped with informatic devices, and training was provided to improve their performance. The experience of the School for Leadership and Peace Building, is currently scaled up by the Government of Nariño in seven other municipalities. Board's members are currently exercising their rights and they are gaining access to social programs. *“Good things have been accomplished with the Secretariat of Education. They now annually give a school kit (notebook, pen, books, etc.) to the boys and girls”,* says a representative of the MPEV from Pasto. This strengthening process promoted the election of a member of de Board of Tumaco to occupy one of the Peace Seats reserved for victim population in the Chamber of Representatives as part of the peace agreement. In Ipiales, actions with public institutions were prioritized to face problems identified thanks to a previous exercise of socioeconomic characterization of victim population. Overall, dialogue between victim communities and public institutions was improved. The result of this is the approval of the MPEV annual plans of the MPEV in a quicker manner, as well as an important increase in public resources assigned to these plans, which have tripled.





PILLAR 2: REINTEGRATION OF FORMER MEMBERS OF THE FARC -EP TO SOCIAL AND ECONOMIC CIVIL LIFE		Target	Progress
2.100	people in the reintegration process improve their capacities for economic-productive insertion, strengthening the social and solidarity economy	1.925	>100%
51	cooperatives or grassroots associations with 2.765 members in reintegration process implementing business units	36	>100%
1.195	people in the reintegration process working on productive projects	1,290	93%
775	people in the reintegration process improve access to basic services	855	91%
130	people in the reintegration process have strengthened their capacities for the effective exercise of citizenship	115	>100%
14	organizations of people in the process of reincorporation engaged in the planning of territorial development	4	>100%
1.646	former combatants have access to land for housing	1.784	92%
1.315	children of ex-combatants cared for by the Colombian care system. This is key to ensuring that their mothers are able to participate in job training and create their own entrepreneurship	2.320	57%
334	former members of FARC-EP with disabilities have been evaluated and are in the process of medical and functional rehabilitation	784	43%

Professionalization of the Multiactive Cooperative Ecomun “Jaime Pardo Leal”

The strengthening of administrative and financial skills of the Cooperative COOJAPAL in the spaces for training and reintegration in Colinas, in Guaviare Department, contributed to the implementation of good accounting and tax practices, as well as transparent, rigorous, and fully documented procurement processes, increasing their legitimacy in the territory. COOJAPAL won two EUTF work tenders because of the quality of their offer, and the fact that they included hiring local workforce. Throughout both contracts, they fulfilled all technical, administrative, and financial obligations, generating employment for 16 people during 5 months. After these successful ventures, the cooperative continued to bid for public tenders for community works. They recently won one in Leticia, in the Amazonas, and were selected by the International Organization for Migration (IOM), to construct one part of a sewer system in the surrounding of Calamar, Guaviare. An agent from the ARN explained: *“They trusted COOJAPAL; all the works turned out very well and complied with all IOM requirements, they worked quickly and responded with high-quality results”*. COOJAPAL is building a portfolio of clients, and they could become a competitive company at regional and national level, with the experience gained with the EUTF.

Cooperative Nueva Esperanza (New Hope Cooperative), a promising initiative in commercialization of coconut

With the aim to boost coconut production, the Cooperative Nueva Esperanza, led by people in process of reincorporation in Tumaco, improved their managerial, administrative and commercial skills, and built a collection center in the region of Río Mejicano. Besides, they signed their first long term agreement with a purchasing company. They increased coconut sales from 14 tons in 2021 to 56,4 tons in 2022. The legal representative of the Cooperative states, *“What we have achieved through this commercial venture is a fair and sure market, allowing to give better prices to our producers”*. Today, this venture enables the creation of three positions (commercial advisor, warehouse assistant, administrative and accounting assistant). Additionally, the need to respond to sales agreements, encourages the hiring of labor to harvest, collect, peel, and select coconut. The Cooperative has earned legitimacy in the territory, several producers from the community have gradually approached the initiative which now has 33 former combatants and 41 rural families. The Cooperative Nueva Esperanza has now a key role as buyer, collector, and marketer in the coconut value chain.



PILLAR 3: INCLUSION: YOUTH, WOMEN, AND ETHNIC GROUPS		Target	Progress
40	young people organizations and rural schools develop projects through Financial Support to Third Parties or other investment mechanisms	16	>100%
2.035	young people have improved their competencies for employability	1.305	>100%
15.160	young people have participated in cultural and territorial identity promotion initiatives	15.850	96%
58	indigenous governments have received technical support for their process of planning and institutional strengthening	77	75%
130	productive initiatives with women strengthened or launched	97	>100%
34	women networks and platforms technically or financially supported to improve their participation and impact in the local and regional public life	30	>100%
445	women are effective members of citizen participation spaces and decision-making boards in the context of local development	695	64%
35	public institutions and civil society spaces have improved their conditions to prevent new cases and assist the victims of gender-based violence (GBV)	9	>100%
850	women victims of GBV assisted by public institutions and/or civil society organization	325	>100%



Chocoamazonic: a dream come true for women from Caquetá

Chocoamazonic is an organization made up of 15 women from El Paujil and La Montañita, in Caquetá. Its focus is cocoa transformation. The EUTF supported the strengthening of their organizational, administrative, technical, and productive skills through technical assistance. Additional support was given to construct a cocoa transformation plant and to improve commercialization and packaging design. To this day, the organization has quadrupled its monthly volume of transformed cocoa, reaching an average of 400 kg and diversifying their products with chocolate bars, powdered cocoa, cocoa butter and bonbons with the highest quality standards, generating a 30% increase in profitability in 2021. This has allowed to employ four persons working 15 days per month, a fourfold increase of wages, continued improvement of plant facilities and proactivity in terms of marketing e.g. by attending fairs and similar events. Chocoamazonic has been able to position itself as a key actor by promoting quality in the price, assisting women in the improvement of post-harvest practices and facilitating the articulation between suppliers with public support programs boosting production. Besides, women have been empowered, have gained economic autonomy and their position in the family has improved. One member of the association states: *“There is no money to be made in homemaking...at home you work, but what you get is what your husband gives you. Now, I work and I contribute, I feel capable, useful. He has no part in it, on the contrary, he says to me: those are your savings, so I go and buy whatever I need”.*

Stronger community network for prevention, detection and first response of gender-based violence

The EUTF helped strengthen the capability for prevention, detection and primary care for women victims of gender-based violence (GBV) of 25 female community leaders belonging to 17 organizations based in 7 municipalities in Putumayo. They autonomously replicated this training in their own communities, reaching a total 100 women and 4 men. By having deeper knowledge of their rights, women in the communities have lost fear to address the subject in public and in their family spheres. *“People nowadays know that cases of GBV must be denounced, (...) there was a lot of violence from the war in this municipality (...). And women thought violence in their homes was violence they could not denounce”*, explains the female leader from the municipality of Orito. Blame of the victims was reduced and trust and solidarity between women increased. Trained female leaders have developed action to raise awareness about gender-based violence reaching other women and young people. Until September 2022, 63 women had been assisted by providing them orientation about their rights, attention routes and, when necessary, psychosocial support. 45 women, received attention from “gender duos” (professional psychologists and lawyers) providing them with information on the cases and avoiding their re-victimization.





PILLAR 4: SUSTAINABLE AND INCLUSIVE PRODUCTIVITY		Target	Progress
5.725	families implementing agroecological practices for self- consumption and local market	5.775	99%
140	infrastructures built or rehabilitated to strengthen agri-food chains	100	>100%
185	organizations develop their own projects through Financial Support to Third Parties or other investment mechanisms	160	>100%
25.770	people have received support to implement sustainable productive models or to strengthen rural economy initiatives	28.660	90%
160	producers' organizations, SMEs, and/or productive units have improved their capacities to access the markets and establish commercial partnerships	130	>100%
485	producers' organizations, SMEs, and/or productive units have received quality certificates or collective marks	875	55%
455	producers' organizations, SMEs, and/or productive units have strengthened their administrative, operative, and commercial processes	555	82%
8.435	people implementing good environmental practices or climate change adaptation/ mitigation strategies in their economic activities	12.095	70%
15.460	hectares implementing or strengthening silvo-pastoral or agroforestry sustainable production models	13.080	>100%
23.290	hectares of terrestrial and aquatic ecosystems recovered and protected by the local communities	14.365	>100%

Sustainable livestock practices reducing pressure on natural resources

With the aim to mitigate productive and economic vulnerability of livestock farmers in the north of Putumayo, and to improve efficiency of productive practices, the EUTF trained 136 families and supported five pilot silvopastoral farms. Sanitary and milking practices were improved, reducing the presence of bacteria in the milk by more than 90%. A total of 390 hectares shifted to a more sustainable farming model dividing paddocks with live fences. Planted trees have improved animal wellbeing providing shade and producing organic materials. There is evidence that livestock farming can be carried out without deforestation, and these practices help to regenerate ecosystems. As one of the beneficiaries stated: *“now grass lasts longer and we have to cut down less from the mountains”*. The rotation of paddocks also helped to improve soils quality, thus increasing the nutritional value of the grass. The quality of forage for the herd was maintained throughout the most adverse climatic periods. All the above resulted in an increased efficiency and production in pilot farms, increasing from an average of 0.5L daily per cow to 1.1L, and a daily increase in steer weight from 0.46kg in average to between 0.8kg and 1kg, thus proving that increased productivity and good environmental practices can be combined.

Sustainable transformation of canangucha to preserve ecosystems

The Association of Rural Women of Colombia and Caquetá (ASMUCOCA) created in 2013, made up of 180 women from La Montañita in Caquetá, produces and commercializes non – timber products, and since 2017 they harvest “canangucha”. In collaboration with the University of Amazonía, the EUTF encouraged capacity building and technical assistance to train these women in the sustainable harvesting of this palm, monitoring canangucha production and managing licenses to harvest 40,2 hectares. Additionally, farms were equipped with cables to improve harvesting, and women in the association were given security equipment to avoid accidents during the process. Today, women from ASMUCOCA see the canangucha as an ecosystem with economic and environmental potential. The President of ASMUCOCA explains: *“Now we are all taking care of the canangucha trees. People no longer burn; they no longer fumigate the surroundings (...) We want to protect and keep protecting”*. The women from ASMUCOCA are nowadays sharing their experiences with other productive associations, thus becoming key actors promoting sustainable development in their territories.





PILLAR 5: ENSURING STATE PRESENCE AND LOCAL GOVERNANCE		Target	Progress
46	territorial institutions receiving technical support on policy planning or institutional strengthening	33	>100%
71	rural schools have aligned their curriculums to the territorial approach	62	>100%
57	community networks and citizen platforms supported to improve their incidence in public life	82	70%
215	infrastructures built or rehabilitated with State and community participation	230	93%
14.180	people from municipalities affected by the armed conflict improving their access to basic public services	17.570	81%

Access to water in rural communities of Tumaco

The EUTF contributed to the improvement of local water management which has been complemented with other public initiatives in Tumaco, Nariño. The EUTF supported the municipal Water and Sanitation Board, improving data for decision making in territorial planning. With the aim to improve access to water in rural areas, two aqueducts were built benefitting 344 people in two villages, increasing public services in Tumaco from 6.84% up to 8.37% and decreasing diarrheal diseases in infants under the age of 5, to around 85%. *“Before, water was collected from the sewage, it was contaminated and we had stomach problems. With the aqueduct, the children not only from my family but from the whole community no longer have such problems”*, explains the President of the community Water Board. Also, aqueducts helped to reduce the price families pay for water, each family currently pays COP 10.000 per month (approximately 2,5 euro). These resources help to pay the salary of the person in charge of maintaining the infrastructure. Traditionally women are being responsible for providing water to their families, training on technical, organizational aspects were provided, and women led the organization of two community Water Boards and managed the construction of two aqueducts. One of the results of these community-managed aqueduct systems has been solving issues related to seasonal water availability.

Encouraging local governance in Guaviare

The EUTF supported five Community Action Boards (CAB) in the municipalities of Calamar, El Retorno and San José del Guaviare, providing them with training, technical and financial assistance (around EUR 435.000) for land planning in 259 plots. Community organizations improved their administrative and management skills and improved accountability. This had an effect on the increase of the Organizational Capacity Index¹, from an average 69,5 to 81,5. Additionally, CABs have incorporated transparency and community participation in all their decision-making processes. The President of the CAB in Las Colinas points out *“The CAB has strengthened their legitimacy because they responded to community requirements. Now they organize meetings and working days with us, as well as bazaars for collecting funds for the community”*. Participative management of resources, including quality control on purchases by the community, has allowed them to have more confidence and reach public entities. Four CABs of Calamar and El Retorno have been supported with municipal and international cooperation subsidies to develop productive projects and social initiatives, such as milk transformation, the maintenance of tertiary roads, training offers and the implementation of spaces for recreation.

1 The Organizational Capacity Index (OCI) is a diagnostic tool to measure an organization's capacity in diverse fields related to the EUTF. This tool is applied at the beginning and the end of organizational strengthening activities.



PILLAR 6: ADDED VALUE OF THE EUROPEAN UNION

The EUTF has transferred specific expertise and experience from EU and EU Member States such as:

- FORLAND, an European tool (open-source platform, dedicated to territorial planning monitoring and decision support), adopted by the Governorate of Guaviare.
- LEADER approach, putting forward European added values related to the promotion of alternative energies, ecotourism, green business and biotrade, river basin development, youth and volunteering, and innovation and technology.
- The focus on commercialisation and markets, achieving the adoption of agricultural practices and certification models complying with European Standards.

The added value of the EUTF relies in two areas: in the political sphere, it has served as an effective platform for the dissemination of democratic values and the principles on which the construction of a lasting peace is based; and in the technical field it has contributed to the strengthening of capacities of the executing and co-executing entities.





Lo único que sentía era vergüenza



Toda la noche lloré, lloré y lloré

2.4. EUTF Visibility

In 2022, EUTF communication focussed on two strategic pillars: **reducing conflict and reconciliation** and social **reincorporation of ex-members of FARC-EP**.

With the aim of visualizing the stories and faces behind the peace process, the event **‘Putumayo: a place of reconciliation and hope’** was organised. It demonstrated various activities building peace, being spearheaded by communities in the region. In 2019 **“Nosotras y El Tigre de Putumayo”** (“Women and El Tigre, Putumayo”) was released. This booklet accompanied by photos vividly illustrates the experiences and suffering of 12 female victims of the massacre committed in El Tigre police district in 1999. Over the course of 2020 and 2021, the virtual exhibition **“Bosquesinas Campesinas”** was aired, showcasing the actions for peace and stewardship of the Amazon Rainforest in Putumayo led by female signatories of the peace agreement and female rural workers.

‘Putumayo: a place of reconciliation and hope’ was attended by Francia Márquez, Vice-President of Colombia, Gilles Bertrand, EU Ambassador to Colombia, the Ambassadors of EU Member States, national allies, representatives of the media, the authorities and important organisations in the region (‘Tejedoras de Vida’ Regional Women’s Alliance and ‘Violetas de Paz’ Women’s Association), in addition to young members of the ‘Tejedoras de Vida’ feminist Batucada percussion band and of the Hosts for Peace programme. It was viewed as the largest communication event organised by the European Union delegation in Colombia

in 2022, portraying Putumayo as a resilient region determined to fight for peace, thus helping to break down prevailing stereotypes about this region. At the same time, it strengthened the position of the European Union as an important ally for building peace in Colombia.

Regarding the social reinsertion of ex-members of FARC-EP, support was given to make the documentary **‘La Montaña’**, produced by signatories of the peace agreement, who are also members of the ‘Miradas Collective’. It shows the collective process of integration into civilian life by signatories of the peace agreement from the former Territorial Training and Reinsertion Space in Anorí, a municipality located in the north-east of Antioquia. EUTF similarly provided support for screening this documentary in the Cinematheque of Bogota, which was attended by the former President of Colombia and Nobel Peace Prize Laureate Juan Manuel Santos, the European Union Ambassador to Colombia, recognised professionals in the art and audio-visual sector, and peace signatories from different parts of the country. This event showed the actual people involved in the reinsertion process in Anorí and also gave impetus to publicising and positioning the Miradas Collective as a creative and innovative force for social and economic reinsertion of signatories of the peace agreement.

The EUTF published **37 articles** on its website during year. Moreover, it recorded **71,701 visits**, 38,104 logins and 23,138 users.



3. Financial report

3.1. Amounts pledged and received

No new amounts were received in 2022.

3.2. Amounts paid

Contract type	Contract Id	Pay. Req. Id	Pay. Type	Paid Amount EUR
Grants in Direct Management	T06.3	T06.141	PN	268.048,34
	T06.4	T06.151	PF	347.445,04
	T06.9	T06.153	PN	360.931,44
	T06.10	T06.161	PN	313.701,92
	T06.24	T06.150	PF	648.769,19
	T06.32	T06.145	PN	57.954,39
	T06.33	T06.154	PF	125.999,69
	T06.39	T06.158	PF	1.061.231,28
	T06.60	T06.160	PF	3.000.005,00
	T06.61	T06.146	PF	1.897.190,00
				8.081.276,29
Procurement in Direct management	T06.7	T06.142	PN	302.977,94
	T06.7	T06.156	PN	245.975,93
	T06.35	T06.143	PN	279.535,60
	T06.35	T06.162	PN	164.662,23
	T06.74	T06.148	PN	135.633,00
	T06.74	T06.163	PN	191.508,00
	T06.77	T06.140	PN	135.950,00
	T06.77	T06.152	PN	137.766,63
	T06.87	T06.144	PN	18.000,00
	T06.98	T06.164	PN	19.450,00
	T06.100	T06.147	PF	69.266,00
	T06.101	T06.155	PN	29.074,00
Indirect management with International Organisations				-
Budget support	T06.73	T06.157		1.500.000,00
				1.500.000,00
TOTAL PAID in 2022				11.311.075,62

3.3. Beneficiaries and amounts contracted²

Number	Title	Contracted amount (EUR)	Paid amount (EUR)	Balance (EUR)	Contractor
T06.2	Rutas para la paz	1.128.903,84	1.128.903,84	0,00	INFIVALLE
T06.4	"Mascapaz"	3.820.000,00	3.149.207,02	670.792,98	INSTITUTO SINCHI
T06.5	"Pazadentro"	2.100.000,00	2.054.338,26	45.661,74	ASOCIACION DE CABILDOS NASA CHA CHA
T06.7	Asistencia técnica para el Fondo	5.772.400,00	3.892.349,35	1.880.050,65	DT GLOBAL IDEV EUROPE S.L.U.
T06.8	Territorios caquetefíos	3.775.965,00	3.345.216,97	430.748,03	INSTITUTO MARQUES DE VALLE FLOR
T06.9	Rural paz	3.630.000,00	3.627.931,44	2.068,56	ICCO COOPERATION
T06.10	PUEDES	3.239.199,75	3.228.981,70	10.218,05	CISP
T06.11	Estabilización puerto Guzmán	1.974.136,00	1.819.724,15	154.411,85	FAO
T06.14	Amazonía joven Guaviare	2.627.730,00	2.619.822,49	7.907,51	FAO
T06.20	PDT nariño	6.500.000,00	6.499.991,00	9,00	AECID
T06.23	Reincorporacion - FAO	2.000.000,00	2.000.000,00	0,00	FAO
T06.24	Caminemos	6.271.679,00	5.644.511,10	627.167,90	ONF INTERNATIONAL
T06.25	Humanicemos	4.000.000,00	3.884.088,91	115.911,09	FAO
T06.28	Colombia PUEDE	2.700.000,00	2.692.348,50	7.651,50	ITC
T06.29	SER putumayo	2.000.000,00	1.800.000,00	200.000,00	CORPOAMAZONIA
T06.33	Constructores de paz	769.998,30	692.998,30	77.000,00	FUNDACION LAZOS DE DIGNIDAD
T06.35	Economías solidarias del común	3.000.000,00	2.400.000,00	600.000,00	LKS-ALECOF
T06.37	MIA	522.000,00	469.800,00	52.200,00	APCO
T06.39	Aremos paz	4.800.000,00	4.078.827,28	721.172,72	FORUM CIV
T06.41	Mujeres que transforman	6.340.000,00	4.590.000,00	1.750.000,00	ICCO COOPERATION
T06.60	Rutas PDET - infraestructura	8.576.398,00	3.874.707,00	4.701.691,00	RED ADELCO
T06.61	Rutas PDET - cadenas	4.609.967,00	2.719.394,00	1.890.573,00	ICCO COOPERATION
T06.62	Rutas PDET - innovacion	6.313.635,00	1.190.496,00	5.123.139,00	CIAT
T06.68	Apoyo presupuestario reincorporacion	10.980.000,00	8.480.000,00	2.500.000,00	REPUBLICA DE COLOMBIA
T06.73	Apoyo presupuestario tierras	9.300.000,00	4.300.000,00	5.000.000,00	REPUBLICA DE COLOMBIA
T06.74	Apoyo complementario a la política de tierras	1.600.000,00	467.141,00	1.132.859,00	ONF INTERNATIONAL
T06.77	Apoyo complementario reincorporacion	2.169.000,00	573.716,63	1.595.283,37	EPTISA SERVICIOS DE INGENIERIA SL*
T06.94	Piscicultura del común	4.443.421,11	2.892.924,87	1.550.496,24	CISP
T06.97	Escuela taller, saberes y patrimonio para la paz	200.000,00	180.000,00	20.000,00	FUNDACION ESCUELA TALLER DE CALI
T06.98	Audit EU Trust Fund Colombia	97.250,00	19.450,00	77.800,00	ERNST & YOUNG BEDRIJFSREVISOREN
T06.99	Verificación de gastos al contrato T06.29	18.710,00	0,00	18.710,00	DELOITTE
T06.100	Evaluación intermedia - EUTF	187.850,00	69.266,00	118.584,00	ALTAIR ASESORES SL
T06.101	Verificación de gastos T06.2	29.074,00	29.074,00	0,00	DELOITTE BEDRIJFSREVISOREN/ REVISEURS D'ENTREPRISES
T06.102	Verificación de gastos T06.9 - ICCO	19.500,00	0,00	19.500,00	BKF INTERNATIONAL SA
T06.104	Verificación de gastos 2 lotes	34.051,00	0,00	34.051,00	MAF AUDITORES SLP
		115.550.868,00	84.415.209,81	31.135.658,19	

² Includes both operational contracts and audit contracts

4. Management and internal control

4.1 Control results

4.1.1. Control effectiveness as regards legality and regularity

4.1.1.1. Results of ex-ante controls

Ex-ante controls demonstrated to be effective with €384,133 of undue payments identified, representing 1.99% of the total amount paid in 2022 for EUTF projects (KPI 23). The important amount of ineligible costs is notably due to budgetary and accounting irregularities (financial reporting), wrong application of tendering and contracting EU procedures and lack of supporting documentation. Because of travel restrictions due to the COVID-19 crisis, especially during the first part of the year, the majority of ex-ante controls took the form of desk reviews, but field visits resumed later in the year to further reinforce the control work.

4.1.1.2. Results of external audits

The financial audits executed in 2022 identified a very high amount of ineligible expenses, totalling € 631,633, representing 20.56% of the total amount audited of €3,071,628 (KPI 27). This important amount of ineligible costs is mainly due to the misuse of tendering/contractual procedures, misinterpretation of rules, lack of documentation and incorrect financial reporting.

It has to be noted that this high amount and percentage still represent a significant decrease compared to the previous reporting year (€ 1,971,599 and 42.85%, respectively). This is due to the mitigating actions that stemmed from the analysis of the situation. The OPER and FCA sections increased their technical and financial support to project beneficiaries in order to

prevent errors and irregularities. The EUD ensured a proper follow-up of auditors' findings, including recovery of undue paid amounts when necessary.

4.1.2. Fraud prevention, detection and correction

In the management of the EUTF, the EUD is following the anti-fraud strategy of DG INTPA. All colleagues forming part of the financial circuits and in supporting roles are informed about this strategy and are aware of their role in fraud prevention, detection and correction.

In the reporting year, one case with a high number and amount of irregularities identified by the auditors was reported to OLAF.

4.2 Observations and recommendations made by Internal Audit Service

Nothing to report.

4.3 Assessment of the effectiveness of the internal control systems/EU Court of Auditors

Internal controls demonstrated to be very effective. Procurement, contractual and financial circuits have been fully respected. Project verification processes (an appropriate mix of audits, ex-ante controls, monitoring, on-the-spot visits)

allowed identifying € 1 million of errors and irregularities in the application of EC procedures (misuse of tendering processes and wrong interpretation of contractual provisions in some projects). During the year, OPER and FCA sections reinforced their support to implementing partners to help them in the application of corrective measures (reorientation or reduction of activities, budgetary reallocations, application of correct procedures, conformity of financial reporting, etc.).

4.4 Conclusions as regards assurance

The resources assigned to the EUTF activities described in the report have been used for their intended purpose. The regularity and the legality of tendering, contractual and financial operations has been ensured. Despite the difficult working conditions as a consequence of the pandemic, operation and financial staff has demonstrated a high level of responsibility and professional commitment. Internal controls, rules and procedures have been correctly applied. The principles of equality of treatment and impartiality have been fully respected. Based on the excellent results achieved and the quality of work performed, reasonable assurance can be given.



5. Declaration of assurance (and reservations)

I, the undersigned, Alberto. MENGHINI, Manager of the European Union Trust Fund for Colombia,

In my capacity as authorising officer by sub-delegation

Declare that the information contained in this report gives a true and fair view³.

State that I have reasonable assurance that the resources assigned to the activities described in this report have been used for their intended purpose and in accordance with the principles of sound financial management, and that the control procedures put in place give the necessary guarantees concerning the legality and regularity of the underlying transactions.

This reasonable assurance is based on my own judgement and on the information at my disposal, such as the results of the self-assessment, ex-post controls, the opinion of the Internal Auditor on the state of control for years prior to the year of this declaration.

Confirm that I am not aware of anything not reported here which could harm the interests of the European Union Trust Fund for Colombia.


Bogotá, 16/02/2023

e-signed

³ True and fair in this context means a reliable, complete and correct view on the state of affairs under the TF.



6. ANNEXES



Annex I: EUTF projects


a) Programmes focusing on economic development of conflict-affected territories

1. Macarena Sostenible con más Capacidad para la Paz - Mascalpaz

General Description

- **Start date: 08/06/2017**
- **End date: 07/01/2024**

Proyecto:	Macarena Sostenible con más Capacidad para la Paz, Mascalpaz
Socio:	Instituto Amazónico de Investigaciones Científicas, SINCHI
Aporte total Unión Europea:	3.820.000 €
Aportes contrapartida:	800.000 €
Cobertura:	4 municipios en el departamento de Meta
	1. Meta, Mesetas, Puerto Rico, San Juan de Arama y Vista Hermosa



The project promotes sustainable and comprehensive rural development contributing to improving living conditions, institutional and organisational strengthening, and lasting peacebuilding in the region.

Among the specific actions to strengthen local economies, the following can be highlighted: protecting the forest and its water resources; improving in public goods; creating educational models for young people; and promoting environmental sustainability and governance for peace with a gender, generational, intercultural, sustainability, and a no-harm approach.

Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of families occupying buffer zones, which advance the processes of tenure ownership	800	0%	0
2 Number of families receiving Technical Assistance and implementing a sustainable productive model	3,200	100%	3,200
3 Number of families that have implemented agrosilvopastoral production in rural farms and dairy producers embracing sustainable livestock	200	100%	200
4 Number of model farms that have implemented a sustainable fish farming model	20	100%	20
5 Number of tourism services providers that, at the end of the project, are positioned in ecotourism as an economic alternative in the four municipalities	20	100%	20
6 Number of hectares resulting from conservation and restoration agreements with farmers in the four municipalities, in order to improve native plant coverage and plant material production in this AMEM area	1,000	>100%	1,140
7 Number of micro-basins in the project area that, at the end of the project, are restored and / or recovered according to the prioritization, regulations and zoning DMI AMEM, ZRC Sustainable Development Plan, and PIMA Macarena Norte	4	100%	4
8 Number of rural families receiving Technical Assistance, and implementing the production of green fertilizers as part of an environmental recycling model effect in 140 farms	2,300	100%	2,300
9 Number of cold chain milk collection centers in San Juan de Arama that benefits at least 250 producers	1	100%	1
10 Number of urban and rural schools that have infrastructure improvement with local materials and innovation	32	0%	0
11 Number of people, from the settlements in the process of humanitarian demining, directly benefited from the construction of a bridge in Santa Helena, as an iconic work of regional integration	2,400	0%	0
12 Number of farmer and indigenous families linked in commercial agreements within the "Region Brand" strategy	400	100%	400
13 Number of organizational processes strengthening environmental leadership and rural identity	30	100%	30
14 Number of farmer community associations indigenous people linked to supply chains from the dairy, specialty coffee and fruit and vegetable sector	18	100%	18
15 Number of schools with initiatives to complement their curriculum with contents that promote rooting and land legalization by the farmer and indigenous population of the project area	10	100%	10
16 Number of children and youth in the AMEM area linked to the regional recognition program through guided excursions	1,600	100%	1,600
17 Number of initiatives of young environmentalists implemented, in green production, alternative energy, and tree planting	24	100%	24
18 Number of initiatives of an environmental, cultural, and educational nature that favor identity and roots in the region	30	100%	30

2. Territorios caqueteños sostenibles para la paz

General Description

- **Start date: 01/01/2018**
End date: 30/06/2022

The Project consolidates regional peace in Caquetá through improving local capacities for production, processing, and commercialization of products such as cacao, non-wood forest products, sugar cane, and coffee, profitably and competitively, under environmental conservation and social inclusion schemes. The project also seeks to promote reconciliation by strengthening the social fabric and community work.

Proyecto: Territorios caqueteños sostenibles para la paz

Socio: Instituto Marqués de Valle Flór, **IMVF**

Aporte total Unión Europea: 3.775.965 €

Aportes contrapartida: 787.150 €

Cobertura: 4 municipios en el departamento Caquetá

1. Caquetá: El Doncello, El Paujil, La Montañita y Solano



Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of families implementing agroforestry systems climate-change resilient	150	>100%	170
2 Percentage of income increase associated with the improvement of crop management and quality of post-harvest technology	15	>100%	37
3 Number of people trained in added-value processes and commercialisation in the framework of the action	50	>100%	80
4 Number of hectares in conservation agreements linked to agroforestry arrangements	200	>100%	1100
5 Number of community infrastructures supported in the framework of the action	4	>100%	14
6 Number of kilometres of roads implemented, rehabilitated, or adapted	15	>100%	21
7 Number of exports and / or national commercialization of products supported by the project	4	>100%	6
8 Number of producers certified or in the certification process	50	>100%	52
9 Number of associated families trained in preservation and propagation of native seeds, for environmental services, food security, and commercialization	40	>100%	55
10 Number of organisations strengthening through adjusted ICO instrument baseline (organisational, accounting and management issues)	15	>100%	31
11 Number of organisations making effective use of the European financing instrument for financial assistance to third parties	30	100%	30
12 Number of victims and / or reincorporated people with capabilities to be incorporated effectively in local economic initiatives	200	100%	200
13 Number of women effectively associated in citizen participation and development processes, promoted by local institutions in prioritized regions	300	>100%	325
14 Number of endowments to community radio stations	1	100%	1
15 Number of partner entities coordinated for comprehensive rural development processes promoted in the action	5	>100%	11
16 Number of families trained in ecosystem management for the use of non-timber forest products	50	100%	50
17 Percentage of new ex-combatants formally associated to the ETCR cooperative based on their participation in economic initiatives supported by the project	10	>100%	11
18 Number of proposals for Financial Aid to Third Parties promoting gender equality and women inclusion	10	100%	10
19 Kilogrammes of products, processed with the project's support, which have been commercialised	6.000	>100%	19.520
20 Number of people associated and actively participating in self-managed savings and credit groups supported by the project	300	>100%	340

3. Proyecto de desarrollo territorial en el departamento de Nariño en condiciones de paz – PDT Nariño

The project develops a multi- sectoral action, creating economic opportunities with criteria for economic, environmental, and social sustainability, with cross-cutting actions in rights, ethnic, community resilience, and regional approaches.

The project promotes development, strengthening actors and institutions in their management, planning, coordination, communication, and participation capacities, as well as in capacities related to economic development policies, water, and basic sanitation, local institutions and spaces for dialogue, and gender equality. The project fosters spaces for dialogue to encourage the participation of civil society, mainly agricultural producers, women, and victims of the armed conflict.

General Description

- **Start date: 19/05/2018**
- **End date: 18/03/2023**

Proyecto:	Desarrollo Territorial en Nariño
Socio:	Agencia Española de Cooperación Internacional para el Desarrollo, AECID
Aporte total Unión Europea:	6.500.000 €
Aportes contrapartida:	1.654.322 €
Cobertura:	3 municipios en el departamento de Nariño
	1. Nariño: Ipiales, Pasto y Tumaco



Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of business units that access technical / financial assistance	52	>100%	57
2 Number of business units that are strengthened	43	100%	43
3 Number of business units improving their infrastructure and equipment	43	>100%	56
4 Number of business units accessing markets	47	>100%	50
5 Number of entities linked to the Regional Entrepreneurship Network (RREN) of Nariño, strengthened in quality and efficiency of their entrepreneur support services	26	>100%	35
6 At least 15 rural educational institutions developing entrepreneurial skills training strategies	15	>100%	23
7 Number of young people trained in traditional trades and human development, linked to productive units (Craft Workshops), under the methodology of School Workshops	25	100%	25
8 Number of strategies or public policies approved in the framework of the project	1	>100%	4
9 Number of people with new or rehabilitated access to drinking water, under the project	320	>100%	530
10 Rural water systems built or rehabilitated under the project	4	75%	3
11 Number of regional entities increasing their planning capacity, quality service and management instruments, within the framework of the project	2	100%	2
12 Number of tools / processes improved in planning and investment in the region to improve the capacities of regional institutions	16	75%	12
13 Percentage of budget supported by a Community Infrastructure Project in a settlement (vereda) nucleus - PIC, under the PDET Tumaco	50	>100%	70
14 Number of life plans developed for strengthening the capacities of ethnic authorities	19	47%	9
15 Number of people participating in regional management public spaces	300	100%	300
16 Number of departmental and municipal victims work groups with management capacity, attending the victims' demands	4	100%	4
17 Number of institutions/ organisations that increase the number of actions in favour of the human rights of women in the department of Nariño	8	100%	8
18 Number of women accessing protection and care measures for women victims of gender-based violence implemented within the framework of the project	100	>100%	300
19 Number of women victims of gender-based violence accessing economic empowerment services implemented under the project	25	60%	15

4. Desarrollo rural integral del Guaviare para la paz – Caminemos Territorios Sostenibles

General Description

- **Start date: 12/06/2018**
- **End date: 21/09/2022**

The project has a differentiated approach, thus supporting initiatives for vulnerable social groups such as women, youth, ex-combatants, and indigenous people. The project improves the economic situation and well-being of the participating communities by making changes in their production systems and preserving their natural environment and resources. Thus, it strengthens food security and individual and organisational capacities, under an inclusive and participatory approach.

Proyecto:	Caminemos Territorios Sostenibles
Socio:	Office National des Forêts, ONF Andina
Aporte total Unión Europea:	6.271.679 €
Aportes contrapartida:	1.306.739 €
Cobertura:	3 municipios en el departamento de Guaviare
	1. Guaviare Calamar, El Retorno y San José del Guaviare



Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of families that have seen an increase their income (including self-consumption cost of opportunity)	180	>100%	1.400
2 Number of grassroots organisations improving their economic, administrative, and / or commercial capacities through the Financial Support to Third Parties instrument	15	>100%	30
3 Number of regional and national public entities making effective use of FORLAND	5	>100%	6
4 Number of families that have done property planning	400	>100%	435
5 Number of families implementing economic alternatives for self-consumption and local commercialization of surpluses	400	100%	400
6 Number of hectares under forest management plans	2.000	>100%	6.290
7 Number of hectares in agroforestry and silvopastoral systems	220	>100%	1945
8 Number of hectares of forest restored	220	>100%	280
9 Number of hectares under conservation agreements	4.000	>100%	13.190
10 Number of families belonging to grassroots organisations that, through Financial Support to Third Parties, are implementing new strategies for quality, value creation, and commercialization	300	>100%	970
11 Number of children and young people who, with EU support, participate in initiatives for peacebuilding, rural development, and strengthening roots	1.000	>100%	1.030
12 Number of debate spaces (forums, events, community radio broadcasts) opened by the project	5	100%	5
13 Number of participants in training workshops in organisational, environmental, and key practices in health and nutrition	1.000	>100%	1605
14 Number of infrastructures used and maintained for access to safe water	2	100%	3
15 Number of people improving or having access to safe water with the project's support	500	96%	485
16 Number of ex-FARC EP combatants participating in collective and / or solidarity economy projects with the EU support	200	>100%	215
17 Number of FARC EP ex-combatants receiving technical training for labor inclusion and / or entrepreneurship with EU support	100	97%	97

5. Colombia PUEDE: Paz y unidad a través del desarrollo productivo y el comercio

General Description

- **Start date: 18/12/2018**
- **End date: 17/09/2022**

The project promotes commercial opportunities through greater participation of producers in local and international markets, and by improving economic productivity, quality, and meeting the market requirements. This is achieved through a set of interventions and investments, as: access to quality standards and certifications, economic infrastructure, technical support and organisational strengthening. The project seeks greater participation of producers in the market, giving added-value to products and meeting market demands.

Proyecto:	Colombia PUEDE
Socio:	International Trade Center, ITC (Centro de Comercio Internacional)
Aporte total Unión Europea:	2.700.000 €
Aportes contrapartida:	667.969 €
Cobertura:	4 municipios en el departamento de Nariño

1. Nariño: Tumaco, Leiva, El Rosario, Policarpa



Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Average monthly income of small farmers (COP)	20	100%	20
2 Number of producers that have adopted agricultural practices improved	500	>100%	730
3 Number of producers reporting better operational and management performance	15	>100%	18
4 Number of producers and organisations that have performed business transactions	800	>100%	1.705
5 Number of producers and organisations that have performed international commercial transactions	10	>100%	11
6 Number of small farmers trained in post-harvest management techniques	1.000	>100%	1.205
7 Number of producers trained in good agricultural practices	800	>100%	855
8 Number of producer organisations trained in negotiation and management	25	80%	20
9 Number of producers trained in entrepreneurship, finance, and collective organisation management	1.500	>100%	1.875
10 Number of producers and organisations reporting greater knowledge in markets and international trade	1.200	>100%	1.235
11 Number of producers with access to tools, guidance, and marketing materials	1.800	100%	1.800
12 Number of producers participating in partnerships in the value chains established during the action Water and sanitation strategies and access to energy	600	>100%	935

6. Implementación de alternativas sostenibles y eco-amigables en el departamento de Putumayo - SER Putumayo

The project supports social and economic reincorporation among local communities and post- conflict actors in Putumayo by developing more sustainable, inclusive and climate-resilient models.

General Description

- **Start date: 24/11/2018**
- **End date: 22/03/2022**

The project also strengthens and stimulates small agricultural producers and former combatants' economic capacities. It does this through sustainable economic alternatives that preserve and strengthen local ecosystems, and through scientific knowledge and technology transfer.

Some of the sustainable technologies transferred to local actors include agroforestry systems, botanical gardens, community nurseries, silvopastoral systems, aquaculture, processing plants, marketing, and ecotourism.

Proyecto:	Alternativas sostenibles y eco amigables para el Putumayo
Socio:	Corporación para el desarrollo sostenible del sur de la Amazonía, Corpoamazonía
Aporte total Unión Europea:	2.000.000 €
Aportes contrapartida:	506.115 €
Cobertura:	6 municipios en el departamento de Putumayo

1. Putumayo: Orito, Mocoa, Puerto Asís, Puerto Guzmán, Puerto Leguizamo y San Miguel



Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of hectares of agricultural and pastoral ecosystems in which sustainable land management practices have been introduced with EU support	400	100%	400
2 Percentage of small producers participating in the project adopting improved technologies	60	100%	60
3 Number of technicians working with the "Training Trainers" methodology	19	>100%	34
4 Number of qualified technicians working as trainers (TOT)	15	>100%	16
5 Number of people participating in technical training	2,000	>100%	2,680
6 Number of processing plants in operation	2	100%	2
7 Number of people implementing Amazonian gardens	115	100%	115
8 Agroforestry and silvopastoral production systems in which sustainable management and conservation practices have been introduced with EU support (number of hectares)	38	100%	38
9 Number of juvenile fish produced in the Corpoamazonía production center ponds	20,000	>100%	29,000
10 Number of clients benefiting from tourist services (accommodation and trails) at ETCR la Carmelita	100	0%	0
11 Number of men and women in the ETCR la Carmelita benefiting from drinking water services	67	100%	67
12 Number of agreements with commercialization agents, including producers, associations, and cooperatives	5	>100%	7
13 Number of people participating in technical tours and / or experience exchanges	7	100%	7

7. Empoderamiento político y económico territorial con enfoque en las mujeres rurales – Mujeres que transforman


General Description




- **Start date: 01/07/2019**
- **End date: 31/03/2024**

In the framework of the Peace Agreement, this action aims to create conditions of well-being for the rural population in the areas most affected by the conflict. In particular, it is the occasion for the women of Putumayo to access and fulfil their rights, participate effectively and with equity in the social and economic life, and being recognized and valued in the transformation that Colombia and Putumayo require.

Proyecto:	Mujeres que transforman
Socio:	Stichting Interkerkelijke Organisatie Voor Ontwikkelingssamenwerking, ICCO
Aporte total Unión Europea:	6.340.000 €
Aportes contrapartida:	0 €
Cobertura:	9 municipios en el departamento de Putumayo

1. Putumayo: Mocoa, Orito, Puerto Asís, Puerto Caicedo, Puerto Guzmán, Puerto Leguizamó, San Miguel, Valle del Guamuez y Villagarzón



Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of women's organisations demonstrating a strengthening of their organisational capacity	100	86%	86
2 Number of municipal women's advisory committees operating in 7 municipalities	7	100%	7
3 Number of women and organisations training and applying tools to build a culture of peace	900	78%	700
4 Number of policies, projects, ordinances and agreements implemented by the department authorities and municipalities aimed at women's empowerment, gender equity and GBV prevention	8	100%	8
5 Number of women's initiatives and their organisations implemented for the political and social empowerment of women	25	72%	18
6 Number of Alliance women formed by Technical Assistance in Leadership, Construction of Social Fabric and Planning and Implementation of Social Action Projects	230	>100%	310
7 Number of women who state that they have sought access to the care route (indigenous women, peasant women, etc.)	230	80%	185
8 Number of actions supported that include women former combatants	2	50%	1
9 Number of women former combatants trained in Leadership, Social Fabric Building and Planning and Implementation of Social Action Projects	30	0%	0
10 Number of economic initiatives led by women that include innovative proposals (good agricultural practices).	20	75%	15
11 Number of people increasing their family income with project support	1.200	96%	1.155
12 Number of people trained in sustainable entrepreneurship management	1.500	>100%	1.890
13 Number of productive initiatives implemented, with seed capital, support, technical and administrative advice, etc.	60	85%	51
14 Nº of initiatives that achieve commercial alliances and strengthen their production chains with in observation the number of organisations	5	>100%	8
15 Number of economic initiatives successfully connected with departmental and national government entrepreneurship/funding policy instruments for rural women and youth	1.000	88%	880
16 Number of rural development's initiatives implemented by municipal and departmental administrations with the final target groups	8	>100%	17
17 Number of producer families accessing market channels through their associations	600	49%	295
18 Number of families implementing alternative non-farm income-generating initiatives	300	>100%	315

8. Estabilización territorial mediante el fortalecimiento de cadenas productivas, mejor acceso a recursos, servicios, infraestructura y mercados – Rutas PDET

The intervention is aligned with the Government’s “Peace with Legality” Policy and gives regional institutions, especially the Territorial Renovation Agency (ART), a central role in implementation, thus fostering institutional coordination. It focuses on value chains: cocoa in Putumayo and Tumaco (Nariño), and dairy in Caquetá, integrating the following lines of action:

General Description

- **Start date: 18/07/2020**
 - **End date: 22/12/2024**
- (i) improve rural roads in areas with potential to develop production chains; (ii) strengthen processing and marketing companies integrated to chains; (iii) promotion to technological innovation applied to value chains; (iv) partnerships between the various steps and actors of the production chains.

In addition, an Investment Fund, a Business Development Services Fund, and a Technical Assistance Facility will be available. In a transversal way, work will be made by applying the gender approach in implementation, to promote women empowerment in the two production chains, with an emphasis on their equitable participation in the expected improvements, and greater control of the processes and benefits created.

Proyecto:	Rutas productivas PDET para la estabilización
Socios Ejecutores:	Red Adelco, ICCO y Centro Internacional de Agricultura Tropical, CIAT
Aporte total Unión Europea:	19.500.000 €
Aportes contrapartida:	3.000.000 €
Cobertura:	9 municipios en los departamentos de Caquetá, Nariño y Putumayo
	<ol style="list-style-type: none"> 1. Caquetá: El Paujil, La Montañita, Puerto Rico y San Vicente del Caguán 2. Nariño: Tumaco 3. Putumayo: Mocoa, Orito, Puerto Guzmán y Villagarzón



Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of companies that have signed co-investment contracts prioritising women-led ventures that meet investment requirements	3	33%	1
2 Percentage of women who are part of the mechanisms of control or social oversight of road infrastructure building	40	0%	0
3 Number of kilometers of roads implemented, rehabilitated or upgraded, and maintained through road infrastructure works	94	14%	13
4 Number of producers trained in new technologies in sustainable livestock systems based on improved fodder including silvopastoral systems and in efficient use of resources	500	47%	240
5 Number of cocoa producers receiving technical training and accompaniment for the adoption of sustainable practices	500	45%	225
6 Number of enterprises benefiting from the investment fund that have increased their sales volume	8	12%	1
7 Number of certified enterprises that meet the requirements to use the “QC” mark	2	0%	0
8 Number of production units certified in good livestock farming practices or in the process of validation	64	0%	0
9 Number of production units certified in good cocoa production practices or in the process of certification	48	0%	0
10 Number of hectares intervened with sustainable livestock systems including silvopastoral systems and cocoa agroforestry systems	450	0%	0
11 Number of new hectares of forest, agroforestry/silvopastoral and restoration systems under voluntary conservation agreements	950	0%	0
12 Number of community “management and maintenance” committees formed that have the capacity and skills to manage road infrastructure works.	8	0%	0

9. Desarrollo rural integral para el fomento de una paz sostenible – Aremos paz

General Description


- **Start date: 06/09/2019**
- **End date: 05/09/2023**

ForumCiv, Diakonia, Act Church of Sweden, FLM, SweFOR, and We Effect, supported by the Swedish Embassy, designed the project recognizing that peacebuilding and the creation of permanence and rooting conditions of the communities in their regions depend not only on material resources, but also on recognition processes, reconciliation, participation, and socio-economic inclusion.

The project combines actions in the fields of sustainable agro-ecological production, and the reconstruction of the social fabric through various strategies that involve the recognition of rural communities as relevant actors in the formulation of public policies, programmes and projects that enable comprehensive rural development, especially those plans included in the implementation of the Peace Agreement such as PATRs⁴.

Proyecto:	Desarrollo rural integral para el fomento de una paz sostenible - Aremos Paz
Socio:	ForumCiv
Aporte total Unión Europea:	4.800.000 €
Aportes contrapartida:	1.200.000 €
Cobertura:	50 municipios en los departamentos de Arauca, Caquetá, Cauca, Cundinamarca, Huila, Guaviare, Meta, Tolima y Valle del Cauca

1. Arauca: 3 municipios	6. Guaviare: 3 municipios
2. Caquetá: 5 municipios	7. Meta: 4 municipios
3. Cauca: 24 municipios	8. Tolima: 3 municipios
4. Cundinamarca: 4 municipios	9. Valle del Cauca: 1 municipio
5. Huila: 3 municipios	

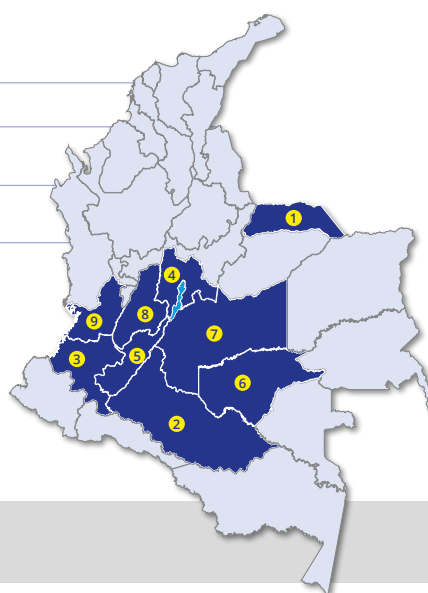

Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of persons trained in protection and non-violent self-protection	150	>100%	1.135
2 Percentage of productive, social and managerial capacity building projects implemented	70	1%	1
3 Percentage of productive projects that receive technical assistance or funds	34	71%	24
4 Number of persons who participate in care experiences	30	>100%	810
5 Number of organisations with improvement plans formulated in terms of administrative managerial and/or political management	34	82%	28
6 Number of women receiving trainings in terms of protection and non-violent self-protection, territorial conservation and defence	280	89%	250
7 Number of agreements between organizations and actors in the business sector, from a local, national and international context	5	0%	0
8 Number of organizations that have received support or advice for their administrative, financial and accounting strengthening	34	82%	28
9 Number of families that thanks to training or methodological transfer processes implement agroecological techniques in their productive activities	1.000	>100%	1.605

10. Apoyo Presupuestario Reforma Sectorial de la Política de Tierras: Tierras y territorios sostenibles para la paz

General Description

- **Start date: 23/12/2020**
- **End date: 30/06/2024**

11. Apoyo complementario Tierras y territorios sostenibles para la paz

General Description

- **Start date: 03/06/2021**
- **End date: 02/12/2024**

This Budget Support contributes to the implementation of the National Land Policy in four municipalities through improved land tenure security and sustainable land use in environmentally sensitive areas.

- This action will support the delivery of land titles, from “vacant territories or baldios” for economic development purposes; and formalization of property rights for those who already have access to land.
- Rural families living in environmental sensitive areas will have the opportunity to secure land rights by using land in a sustainable way. For that, “right-of-use” contracts will be awarded, individually or collectively, setting out the conditions for sustainability.
- The National Land Agency will support families benefiting from land access and land formalization to complement intervention with other income generating projects and programmes from other ministries and agencies.

Proyecto:	Apoyo Presupuestario Tierra y Territorios Sostenibles para la Paz
Socios ejecutores:	Agencia Nacional de Tierras, Office National des Forêts, ONF Andina e Instituto Geográfico de Francia, IGN
Aporte total Unión Europea:	11.000.000 €
Aportes contrapartida:	0 €
Cobertura:	4 municipios en los departamentos de Caquetá y Meta

1. Caquetá: Cartagena del Chairá y San Vicente del Caguán
2. Meta: La Macarena y Uribe



B) Programmes focusing on reincorporation of ex FARC combatants

12. HUMANICEMOS DH: Mecanismo de reinserción social y económica de excombatientes de las FARC-EP a través de actividades de Desminado Humanitario

General Description

- **Start date: 18/12/2018**
- **End date: 17/09/2022**

The project promotes three Humanicemos DH areas:

1. Specialized training and employment creation for former FARC-EPs former combatants in the action against mines.
2. Actions for prevention and reconciliation with communities
3. Knowledge generation to systematize, replicate, and escalate the actions included in the Peace Agreement.

It contributes to socio-economic reintegration, strengthens Colombia's response to the scourge of anti-personnel mines, and creates opportunities for reconciliation with affected communities. It strengthens the capacity of the national sector of action against mines, recognized by the transitional justice mechanism as a form of reparation to victims in conflict-affected areas.

Proyecto:	Humanicemos
Socio:	Servicio de las Naciones Unidas de Acciones contra las Minas, UNMAS
Aporte total Unión Europea:	4.000.000 €
Aportes contrapartida:	0 €
Cobertura:	2 municipios en el departamento de Caquetá

1. Caquetá: La Montañita y Solita



13. Constructores de paz: una estrategia de reincorporación social y económica para la reconciliación y fortalecimiento del desarrollo local


General Description



- **Start date: 16/01/2019**
- **End date: 31/06/2023**

This project contributes to the social and economic reincorporation of ex-combatants in Fonseca and Manaure, promoting reconciliation within the community. Its strategy is based on the development of economically-oriented projects in the construction sector with a comprehensive, differentiated, inclusive, and regional approach.

The Project contributes to improving the conditions for the reincorporated population, strengthening the construction sector and employability in the border region. Moreover, it benefits the population of both ETCRs, their families, and the community through training programmes that promote employment. Subsequently, the implementation of construction sector business units will benefit ex-combatants and the community, who will be employed and will obtain a source of income.

Proyecto:	Constructores de paz
Socio:	Fundación Lazos de Dignidad, FLD
Aporte total Unión Europea:	769.998 €
Aportes contrapartida:	69.999 €
Cobertura:	2 municipios en los departamentos de Cesar y La Guajira
	1. Cesar: Manaure 2. La Guajira: Fonseca



Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 350 ex-combatants and their families have found economic strategies for their economic insertion	350	38%	135
2 30 people from nearby communities have obtained social and economic conditions to access the economic insertion	30	36%	11
3 Three cooperatives, representing 90% of ex-combatant men and women, are consolidated and strengthened, and operate in solidarity economy and collaborative work schemes	3	66%	2
4 Ten permanent spaces for dialogue, joint work and integration between ex-combatants, families, and nearby communities available for community integration and reconciliation	10	>100%	12
5 200 men and women have been trained in sustainable construction and eco architecture	200	>100%	265
6 200 women have acquired knowledge and skills necessary to undertake social / solidarity economy and sustainability initiatives that contribute to local development	200	100%	200
7 160 ex-combatants and 20 people from the surrounding communities have participated implementing the sector's economic units	180	>100%	230
8 200 men and women have received training in hardware skills, carpentry, brick production, locksmithing, and material transportation	200	>100%	265
9 160 ex-combatants working and being employed in the area of hardware, carpentry, brick production, locksmithing, and material transportation	160	48%	77
10 Four economic units of the construction sector operating permanently in the ETCR and communities	4	>100%	10
11 70% the products are commercialized in the local market	70	>100%	100
12 Two community infrastructures built collectively for reconciliation, reparation, and local development and the well-being of the surrounding and reincorporated population	2	>100%	7
13 90% of ex-combatants, their families, and communities use community infrastructure for social, cultural, and economic activities	90	>100%	100

14. Reincorporación social y económica con enfoque territorial, comunitario y de economía solidaria – Comunidades de economía solidaria


General Description

- **Start date: 14/12/2018**
- **End date: 13/06/2023**

The project's main purpose is to organisationally strengthen ECOMUN and its base cooperatives. This will help ECOMUN develop sustainable economic ventures, create income under an associative and solidarity scheme, and enable cooperatives to position themselves as benchmarks in equitable and equal development. To this end, the project uses the knowledge and practices of LKS-ALECOP, and cooperatives belonging to the Mondragon Group, whose experience and methodology can be very useful in peacebuilding, collective reincorporation, and the development of equitable communities and regions.

Proyecto:	Comunidades de economía solidaria y fortalecimiento de ECOMUN y sus cooperativas
Socio:	LKS - ALECOP
Aporte total Unión Europea:	3.000.000 €
Aportes contrapartida:	0 €
Cobertura:	22 municipios en 12 departamentos:

- | | |
|---|--|
| 1. Antioquia: Anorí, Dabeiba, Ituango y Remedios. | 6. Guajira: Ponedores |
| 2. Arauca: Arauquita | 7. Guaviare: San José del Guaviare |
| 3. Caquetá: La Montañita y San Vicente del Caguán | 8. Meta: La Macarena, Mesetas y Vistahermosa |
| 4. Cauca: Buenos Aires, Caldono, Miranda y Patía | 9. Nariño: Tumaco |
| 5. Cesar: La Paz | 10. Norte de Santander: Tibú |
| | 11. Putumayo: Puerto Asís |
| | 12. Tolima: Icononzo y Planadas |

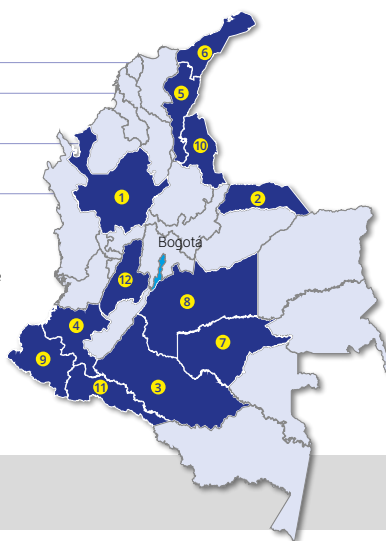

Indicators achieved up to 2021⁵

Indicator	Goal	Progress	Current Value
1. Number of strategic and management plans, agreed and executed, for the development of the ECOMUN Corporation	4	75%	3
2. Number of bylaw documents (congressional norms, regional groups, and base cooperatives) validated by ECOMUN, in accordance with the cooperative laws in force	3	>100%	30
3. Number of ETCRs and NARs participating in communication dynamics for the cooperative model, the bylaws, among others.	60	86%	52
4. Number of people trained in organisational and economic aspects (disaggregated by gender, ethnicity and / or disability)	600	47%	285
5. Number of cooperatives that remain associated with ECOMUN as a consequence of the different socialization processes	70	>100%	155
6. Number of ordinary and / or extraordinary assemblies of base cooperatives to analyze, debate, make proposals for modification, and approve the bylaws at their different levels	80	>100%	90
7. Number of cooperatives that, being part of ECOMUN, receive advice and technical assistance from ECOMUN and / or LKS- ALECOP, improving their cooperative vision and management capacities	70	0%	0
8. Number of strategic plan chains, integrating the management responsibilities of ECOMUN, regional divisions, and grassroots cooperatives	4	0%	0
9. Number of partnerships established by ECOMUN with the project's support, allowing the commercialization of products or services from the basic cooperatives	8	0%	0
10. Number of proposals, models, and approaches that can reinforce the development of value chains in an integrated way, including financing models	2	0%	0
11. Number of events attended and / or participated by ECOMUN as a speaker to develop business relationships and / or develop the brand image	4	0%	0
12. Number of grassroots cooperatives participating in production or commercial chains led by ECOMUN	60	0%	0

⁵ No information available beyond June 2021.

15. MIA: Programa de desarrollo socioeducativo para la mujer desmovilizada del conflicto armado en Colombia (Mestiza, Indígena, Afrodescendiente)

General Description

- **Start date: 10/04/2019**
- **End date: 09/03/2023**

The project strengthens and complements the processes already started by the base organisations in the training and economic sphere. The project reinforces aspects of the reincorporation process regarding inclusion economic, social, and political issues of ex-combatant women and their communities. This is done by: strengthening women’s collective entrepreneurship; developing solidarity economy and care actions; and encouraging political participation, with an explicit differentiated approach that promotes the empowerment and integration of ETCRs with surrounding communities.

Proyecto:	MIA: Mestiza, Indígena y Afrodescendiente
Socio:	Acción Cultural Popular, ACPO
Aporte total Unión Europea:	522.000 €
Aportes contrapartida:	58.000 €
Cobertura:	5 municipios en los departamentos de Caquetá y Chocó
	<ol style="list-style-type: none"> 1. Caquetá: Florencia, La Montañita, Puerto Rico y San Vicente del Caguán 2. Chocó: Carmen del Darién



Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of women integrating in spaces for participation and / or decision-making mechanisms within targeted ETCRs and communities where there is reincorporation of ex-combatants, and surrounding communities	15	66%	10
2 Number of ex-combatant women who have an economic activity (formal, informal, or self-employment)	100	99%	99
3 Women participants in rural communication and journalism workshops	62	91%	57
4 Number of women who have acquired citizenship competencies through training	85	>100%	99
5 Number of viable projects formulated and self-managed by ex-combatant women or women leaders from the surrounding communities	6	0%	0
6 Number of productive initiatives in which women have an organizational management role	6	>100%	8
7 Number of commercialization plans by ETCR and in other reincorporation spaces	6	0%	0
8 Number of ex-combatant women and leaders of neighboring communities with access to technical agricultural studies	20	100%	20
9 Number of agreements with local community media and / or networks, collectives, managed by women ex-combatants for each targeted region	3	0%	0
10 Number of academic or commercial events involving ex-combatant women from targeted ETCRs and other reincorporation spaces	5	80%	4
11 Number of women from ETCRs or neighboring areas who are members of the leader women network	12	100%	12
12 Number of exchanges and/or alliances between the 3 targeted ETCRs and with other ETCRs	4	0%	0
13 Community communication systems equipped and operating at the ETCR in Caquetá	2	50%	1

16. Apoyo Presupuestario Reforma Sectorial de la Política Nacional de Reincorporación Social y Económica de exintegrantes de las FARC-EP (PNRES)

General Description

- **Start date: 07/05/2020**
- **End date: 06/05/2024**

17. Asistencia técnica al Apoyo Presupuestario a la Política Nacional para la Reincorporación Social y Económica de exintegrantes de las FARC-EP

General Description

- **Start date: 05/05/2021**
- **End date: 04/05/2024**

This Budget Support contributes to the implementation of the National Policy for Social and Economic Reincorporation of FARC-EP ex-members. This support will contribute to the implementation of the entire reincorporation policy, that is:

- Improve coordination and planning between the actors involved in the process of comprehensive reincorporation of former FARC-EP members and their families.
- Strengthen the social fabric, coexistence and reconciliation, at the local level and with a focus on communities.
- Social and economic reincorporation of former FARC-EP members and their families, according to their interests, needs, and potential.
- Strengthen human rights of ex-combatants and their families.

People's rights, gender equality, and the approach of empowering the most vulnerable (women, children and people with disabilities) are instrumental in this action.

Proyecto:	Apoyo a la Reincorporación Social y Económica de ex integrantes de las FARC - EP
Socio Líder:	Consejería Presidencial para la Estabilización y la Consolidación
Aporte total Unión Europea:	10.980.000 €
Coordinación:	Agencia para la Reincorporación y la Normalización, ARN
Otras entidades participantes:	Agencia Nacional de Tierras, Departamento Nacional de Planeación, Instituto Colombiano de Bienestar Familiar, Ministerio de Salud y Protección Social, Ministerio de Vivienda, Ciudad y Territorio, Servicio Nacional de Aprendizaje - SENA y demás entidades con responsabilidades en la Política de Reincorporación.
Cobertura:	Nacional Población ex combatiente FARC - EP en proceso de reincorporación



18. Piscicultura del Común

General Description

- **Start date: 09/09/2021**
- **End date: 08/09/2024**

This Fish farming project contributes to the development of solidarity and peacebuilding through the socioeconomic reincorporation of FARC ex-combatants. This project is coordinated through different regional fish farming development networks that supply internal needs, local and regional markets and that have the potential to participate in specialized national and international markets.



Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of persons associated to Ecomún with capacities to successfully manage the fish farming business	250	15%	39
2 Number of persons in reincorporation who improve their access to basic services	24	16%	4
3 Number of constructed and/or adapted fish farming unit in operation	7	28%	2
4 Number of established business partnerships	7	0%	0
5 Number of formalized fish farming units in terms of environmental, productive and sanitary terms	7	42%	3
6 Number of established business plans	7	0%	0
7 % of producers complying with good environmental and safety management practices in fish production	70	12%	9
8 Tons of fish produced during the last year	925	6%	55
9 Number of fingerlings produced during the last year	2.500.000	12%	320.000
10 Variation of the productivity index of the fish farming model in the production units	35	43%	15
11 Tons of fish processed and traded	927	5%	44
12 Number of traded fingerlings	1.200.000	6%	72.735
13 Variation in the profitability index of the fish farming business	1,20	67%	0,81

19. Taller Escuela: Saberes y patrimonio para la paz


The objective of the project is to develop productive capacities of 175 ex-combatants and 25 people from communities affected by the conflict, using a 'learning by doing' methodology. The main expected results are:

General Description

- **Start date: 15/12/2021**
- **End date: 14/04/2023**

- Three technical trainings (gardening and bioconstruction) and three complementary trainings (graphic production and gardening) organised for the target group.
- Improved employability, with an aim of 60% of participants becoming employed at the end of the project.
- Promotion of local production through artisan workshops (Talleres Escuela Artesanales) together with cooperatives organised by ex-combatants.
- Ten strategic alliances formed to improve sustainability and commercialization of production.
- Enhancement of cultural and natural heritage to promote its safeguarding, correct adoption, and sustainable use.

Proyecto:	Taller Escuela: Saberes y patrimonio para la paz
Socio:	Fundación Escuela Taller de Cali
Aporte total Unión Europea:	200.000 €
Aportes contrapartida:	0 €
Cobertura:	6 municipios en los departamentos de Cauca, Huila, Tolima y Valle del Cauca 1. Cauca: Santander de Quilichao 2. Huila: Neiva 3. Tolima: Ibagué y Planadas 4. Valle del Cauca: Cali y Tuluá

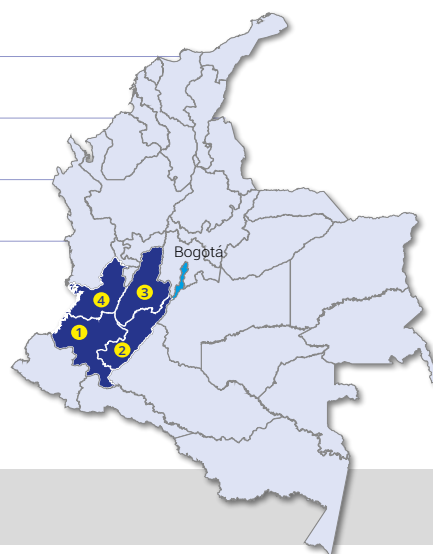

Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of participants certified as construction technicians with emphasis on bio-construction	32	21%	7
2 Number of participants certified as garden technicians	28	67%	19
3 Number of people trained in the appropriate workshops and equipped as "Living Museums"	40	75%	30
4 Number of people trained in graphic design	20	0%	0
5 % of employed beneficiaries % of employed beneficiaries	60	11%	7
6 Number of commercial partnerships	10	0%	0

C) CROSSCUTTING SUPPORT AND AUDITS


20. Technical Assistance to the European Trust Fund of the European Union in Colombia- T06.7

General Description

- **Start date: 08/11/2017**
- **End date: 07/05/2024**

This action provides technical assistance to EUTF Projects and to the EUTF itself. Activities include monitoring and evaluation of projects, communication and visibility support, logistical support, technical expertise and support in project formulation, document drafting, studies, etc), as well as capacity building and support to implementing partners.

Proyecto:	Asistencia Técnica al Fondo Europeo para la Paz
Socio:	AECOM / DT -GLOBAL
Aporte total Unión Europea:	5.772.400 €
Aportes contrapartida:	0 €
Cobertura:	Nacional

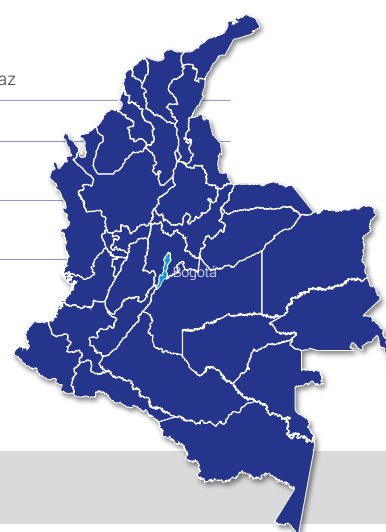

Indicators achieved up to 2022

Indicator	Goal	Progress	Current Value
1 Number of projects of the European Fund for Peace supported through Technical Assistance	31	100%	31
2 Number of expert-days provided to support the European Fund for Peace	6,380	84,5%	5.392,5
3 European Fund for Peace quantitative and qualitative monitoring reports prepared for the visibility and dissemination of progress and learning	21	71%	15
4 Number of visibility and strategic communication manuals prepared by the Technical Assistance	29	>100%	31

21. Audit of Trust Fund 2017 – 2022

On 2022, 5 new contracts have been signed, 1 audit and 4 expenditure verification ones.

Number	Contract Title	Amount EUR
T06.98	Audit EUTF	97.250
T06.99	Expenditure verification, T06.29, Serputumayo	18.710
T06.101	Expenditure verification T06.2	29.074
T06.102	Expenditure verification T06.09	19.500
T06.104	Expenditure verification T06.24 y T06.35	34.051
	Total	198.585



Annexe II

List of derogations, exceptions, non-compliance events, prior approvals and events to be reported

In 2022, the EUTF Manager granted exceptions for the awarding of contract services (mainly audits and one evaluation) under a negotiated procedure to particular service providers, for technical reasons.

EUTF COLOMBIA - DEROGATIONS, EXCEPTIONS AND NON-COMPLIANCE EVENTS - YEAR 2022									
Exceptions									
No	Exception	Project title	Contract Number	Type of Contract	Implementing partner	SDAO ⁶ reporting responsibility	Date of signature	Name AOS ⁷	ARES REF.
1	25 d)	EUTF mid-term evaluation	T06.100	Service	Altair Asesores	EUTF Manager	04/02/2022	Rocco Busco	Ares(2022)877 991 del 07.02.2022
2	25 h)	Audit T06.2	T06.101	Service	DELOITTE	HoD	08/07/2022	Gilles Bertrand	Ares(2022)504 7733 del 11.07.2022

6 SDAO: Sub Delegated Authorizing Officer

7 AOS: Authorizing Officer by Sub Delegation

Annex III: List of EUTF Projects

No.	Contract N°	Short name	Full name	Implementing partner	CTR Type	Start Date	End Date	Department
1	T06.2	Rutas para la paz	Rutas para la paz	Instituto Financiero para el Desarrollo del Valle del Cauca, INFIVALLE	Grant	18/04/2017	01/07/2021	Valle del Cauca
2	T06.3	Fronteras de paz	Fronteras de selva y mar para la paz	Instituto de Investigaciones Ambientales del Pacífico, IIAP	Grant	07/04/2017	06/01/2021	Choco
3	T06.4	Mascapaz	Macarena Sostenible con más Capacidad para la Paz, Mascapaz	Instituto Amazónico de Investigaciones Científicas, SINCHI	Grant	08/06/2017	07/01/2024	Meta
4	T06.5	Pazadentro	Pazadentro: Madre tierra, Buen vivir y Paz	Asociación de Cabildos Indígenas Nasa Cha-Cha	Grant	09/05/2017	08/12/2020	Cauca
5	T06.7	Asistencia Técnica EUTF Colombia	Asistencia Técnica para el Fondo Fiduciario para Colombia de la Unión Europea	DT Global	Services	08/11/2017	07/05/2024	National
6	T06.8	Territorios Caqueteños	Territorios caqueteños sostenibles para la paz	Instituto Marqués de Valle Flór, IMVF	Grant	01/01/2018	30/06/2022	Caquetá
7	T06.9	Rural paz	Organizaciones étnico- territoriales y campesinas se fortalecen como agentes centrales en la construcción de la paz y la transformación territorial	Stichting Interkerkelijke Organisatie Voor Ontwikkelingssamenwerking, ICCO	Grant	15/02/2018	30/11/2021	Putumayo, Nariño
8	T06.10	PUEDES	La Paz Única Esperanza para el Desarrollo Económico y Social - PUEDES	Comitato internazionale per lo sviluppo dei popoli, CISP	Grant	30/12/2017	29/12/2021	Putumayo
9	T06.11	Estabilización económica y social del municipio de Puerto Guzmán	Implementación de Acciones para la Estabilización Económica y Social del Municipio de Puerto Guzmán- Putumayo como Contribución a la Construcción de Paz Estable y Duradera	Food and Agriculture Organisation of the United Nations, FAO	Delegation agreement	01/05/2018	31/12/2021	Putumayo
10	T06.13	Colombia 2020	Pedagogía para la paz: Colombia 2020	El Espectador	Services	1/03/2018	31/01/2021	National
11	T06.14	Amazonía joven Guaviare	Amazonía joven: Corredores amazónicos sostenibles para la paz liderados por jóvenes en el departamento de Guaviare	Food and Agriculture Organisation of the United Nations, FAO	Delegation agreement	01/06/2018	31/10/2021	Guaviare

No.	Contract N°	Short name	Full name	Implementing partner	CTR Type	Start Date	End Date	Department
12	T06.16	Poder mujer	Empoderamiento político y económico territorial con enfoque en las mujeres rurales	Cáritas Alemania	Grant	16/03/2018	30/06/2019	Putumayo
13	T06.17	Amazonía joven Caquetá	Corredores amazónicos sostenibles para la paz liderados por jóvenes en el departamento de Caquetá	Corporación Manigua	Grant	18/04/2018	30/06/2021	Caquetá
14	T06.17	PDT-Nariño	Proyecto de desarrollo territorial en el departamento de Nariño en condiciones de paz	Agencia Española de Cooperación Internacional para el Desarrollo, AECID	Delegation agreement	19/05/2018	18/03/2023	Nariño
15	T06.22	Radios Comunitarias	Radios comunitarias para la paz y la convivencia.	Red de medios de comunicación comunitarios de Santander limitada, RESANDER	Grant	22/05/2018	18/03/2023	Caquetá, Guaviare, Putumayo, Nariño
16	T06.23	FAO – Integración	Procesos de integración socioeconómica y colectiva como estrategia de dinamización comunitaria y construcción de paz en territorios afectados por el conflicto	Food and Agriculture Organisation of the United Nations, FAO	Delegation agreement	19/05/2018	18/06/2021	Guajira, Cesar, Antioquia, Nariño
17	T06.24	Caminemos Territorios Sostentibles	Desarrollo rural integral del Guaviare para la paz	Office National des Forêts, ONF	Grant	12/06/2018	21/09/2022	Guaviare
18	T06.25	HUMANICEMOS	Humanitarian Demining	The United Nations Mine Actions Service, UNMAS	Grant	06/02/2020	05/07/2022	National
19	T06.27	Apoyo psicosocial	Desarrollo de capacidades para el apoyo psicosocial: fortalecimiento de los profesionales colombianos para proporcionar servicios psicosociales	Society for Psychological Assistance, SPA	Services	01/08/2018	31/07/2020	Cundinamarca, Antioquia, Valle, Córdoba
20	T06.28	Colombia PUEDE	Colombia PUEDE: Paz y unidad a través del desarrollo productivo y el comercio	International Trade Center, ITC	Delegation agreement	18/12/2018	17/09/2022	Nariño
21	T06.29	SerPutumayo	Implementación de alternativas sostenibles y ecológicas, en el departamento de Putumayo	Corporación para el Desarrollo Sostenible del Sur de la Amazonia, CORPOAMAZONÍA	Grant	24/11/2018	23/03/2022	Putumayo
22	T06.32	Tejidos	Fortalecimiento del tejido organizativo local para la reincorporación y la reconciliación	ForumCiv	Grant	01/02/2019	30/09/2021	Putumayo, Cauca, Tolima, Arauca

No.	Contract N°	Short name	Full name	Implementing partner	CTR Type	Start Date	End Date	Department
23	T06.33	Constructores de paz	Constructores de paz: Una estrategia de reincorporación social y económica para la reconciliación y fortalecimiento del desarrollo local.	Fundación Lazos de Dignidad, FLD	Grant	16/01/2019	31/01/2023	Cesar, Guajira
24	T06.34	Territorios solidarios y sostenibles	Fortalecimiento de organizaciones de economía solidaria para el desarrollo de iniciativas económicas y productivas en Espacios Territoriales de Capacitación y Reincorporación	Corporación Mundial de la Mujer Colombia, CMMC	Grant	01/03/2019	23/04/2021	Tolima, Guaviare, Meta
25	T06.35	Economías Solidarias del Común	Reintegración económica y social con un enfoque de economía comunitaria, territorial y solidaria.	LKS - ALECOF	Services	14/12/2018	13/06/2023	26 ETCR in 13 Depts
26	T06.36	Piscicultura del Común	Piscicultura del Común	Fundación Agirre Lehendakaria Fundazioa	Services	09/04/2019	30/06/2021	26 ETCR in 13 Depts
27	T06.37	MIA	MIA: Programa de desarrollo socioeducativo para la mujer desmovilizada del conflicto armado en Colombia (Mestiza, Indígena, Afrodescendiente)	Acción Cultural Popular, ACPO	Grant	11/04/2019	10/03/2023	Caquetá, Choco
28	T06.39	Aremos Paz	Desarrollo rural integral para la promoción de la paz sostenible.	ForumCiv (Formerly Forum Syd Enskilda org:s bistandssamverkan)	Grant	06/09/2019	05/09/2023	Arauca, Tolima, Meta, Guaviare, Cauca, Caquetá, Huila
29	T06.41	Mujeres que transforman	Empoderamiento político y económico territorial con enfoque en las mujeres rurales	Stichting Interkerkelijke Organisatie Voor Ontwikkelingssamenwerking, ICCO	Grant	01/07/2019	31/03/2024	Putumayo
30	T06.60	Rutas PDET	Rutas PDET	Red Adelco	Grant	18/07/2020	17/07/2024	Caquetá, Nariño (Tumaco) and Putumayo
31	T06.61			ICCO	Grant	01/08/2020	31/07/2024	
32	T06.62			CIAT	Grant	23/12/2020	22/12/2024	
33	T06.68 (T06.44)	Apoyo Presupuestario Reincorporación	CERS de la Política Nacional para la Reincorporación Social y Económica de exintegrantes de las FARC-EP	ARN	Budget Support	07/05/2020	06/05/2024	National

No.	Contract N°	Short name	Full name	Implementing partner	CTR Type	Start Date	End Date	Department
34	T06.73 (T06.71)	Apoyo Presupuestario	Contrato de Ejecución de Reforma Sectorial (CERS) "Tierra y Territorios Sostenibles para la Paz"	Government of Colombia	Budget Support	23/12/2020	22/12/2024	National
35	T06.74	Apoyo Presupuestario Tierras	Budget Support- Contrato de Ejecución de Reforma Sectorial "Tierra y Territorios Sostenibles para la Paz"	Government of Colombia	Service	03/06/2021	02/12/2024	National
36	T06.77	Apoyo Complementario APS Tierras	Apoyo Complementario al contrato de Ejecución de Reforma Sectorial "Tierra y Territorios Sostenibles para la Paz"	ONF Andina	Services	03/06/2021	02/12/2024	Caquetá, Meta
37	T06.94	Piscicultura del Común	Piscicultura del Común	Comitato Internazionale per lo Sviluppo dei Popoli, CISP	Grant	09/09/2021	08/09/2024	National
38	T06.97	Taller Escuela	Taller Escuela: Saberes y patrimonio para la paz	Fundación Escuela Taller de Cali	Grant	15/12/2021	14/04/2023	Cauca, Huila, Tolima and Valle del Cauca



UNIÓN EUROPEA

Más información en:

www.fondoeuropeoparalapaz.eu

Y en redes sociales:

#FondoEuropeoParaLaPaz y #EuropacreeEnColombia
